BRUHAT BENGALURU

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Improvements to Roads and drains at Maruthi Saw mill road s
	Consultants	:	Civil Pro
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	30-Jan-21
	Project End Date	:	30-May-21
	Project Length in Months	:	120 Days

Sl. No	*Assignment*	*Unit*	*Modified Schedule B QTY*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Dismantling of existing structures like culverts,bridges, retaining walls and other structure comprising of masonry, cementconcrete, wood work, steel work, including T&P and scaffolding wherevernecessary, sorting the dismantled material, disposal of	Cum	43.88	43.88	100	03-02-21	13-02-21	10
2	Dismantling of existing structures like culverts, bridges, retaining walls and other structure comprising of masonry, cement concrete, wood work, steel work, including T&P and scaffolding wherever necessary, sorting the dismantled material, disposal of unserviceable material and stacking the serviceable	Cum	21.94	21.94	100	08-02-21	18-02-21	10
3	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications and as per the directions of the Engineer-	Cum	1773.07	1773.07	100	05-02-21	07-03-21	30
4	Providing and laying Plain cement concrete of mix1:3:6 with OPC cement @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in foundation mechanically mixed, placed in foundation and compacted by vibration including curing	Cum	606.57	606.57	100	08-02-21	27-05-21	108
5	Providing laying plain/ reinforced cement concrete for side Drains Using M20 nominal mix Concrete with OPC at 300kgs.With 20mm and Down size granite metal coarse aggregate at 0.69cum and fine aggregate at 0.43cum Machne mixed, well compacted for wall and Bottom including centering	Cum	584.69	584.69	100	18-02-21	30-03-21	40

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

MAHANAGARA PALIKE

rrounding area roads in ward no 06 Thanisandra

Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21



100% Complete

100% Complete



100% Complete



100% Complete



100% Complete

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24

CIVIL P.D
Sig.....
Date.....
BANGALORE

BRUHAT BENGALURU

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Improvements to Roads and drains at Maruthi Saw mill road s
	Consultants	:	Civil Pro
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	30-Jan-21
	Project End Date	:	30-May-21
	Project Length in Months	:	120 Days

Sl. No	*Assignment*	*Unit*	*Modified Schedule B QTY*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
6	Providing T.M.T bars Fe 500 steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary	Tonne	39.69	39.69	100	13-02-21	25-03-21	40
7	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,loading,unloading,lead and lift,transportation etc ,copmplete. and as	Sqm	1186.79	1186.79	100	02-04-21	12-05-21	40
8	Providing and Fixing pre cast covering Slab 250mm thick made out of CC 1:2:4 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of alll materials, labour,hire charges of machinery, loading, unloading, lead and lift, transportation etc ,complete. and as	Sqm	140.52	140.52	100	07-04-21	17-05-21	40
9	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum and fine aggregtes @ 0.53cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and	Cum	13.99	13.99	100	12-04-21	22-05-21	40
10	Providing and fixing pre cast solid cement concrete kerb stones made out of CC 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting including formwork, curing, including	Nos	1555.00	1555.00	100	12-04-21	22-05-21	40
11	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour Complete as per specifications and directions of the Engineer in charge.	Sqm	279.80	279.80	100	15-04-21	25-05-21	40

MAHANAGARA PALIKE

rrounding area roads in ward no 06 Thanisandra

Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21



100% Complete

100% Complete



100% Complete



100% Complete

100% Complete

100% Complete

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

CIVIL Pro
Sig.....
Date.....
BANGALORE

BRUHAT BENGALURU

Clients Name	:	Executive Engineer Byatarayanapura Division
Project Name	:	Improvements to Roads and drains at Maruthi Saw mill road s
Consultants	:	Civil Pro
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	30-Jan-21
Project End Date	:	30-May-21
Project Length in Months	:	120 Days

Sl. No	*Assignment*	*Unit*	*Modified Schedule B QTY*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
12	Dismantling of cement concrete pavement by mechanical means using pneumatic tools, breaking to pieces not exceeding 0.02 cum in volume and stock piling at designated locations and disposal of dismantled materials stacking	Cum	191.22	191.22	100	23-04-21	13-05-21	20
13	Excavation for roadwork in all types of soil by mechanical means including cutting and loading to tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross sections, and transportation with a	Cum	856.09	856.09	100	24-04-21	29-05-21	35
14	Compaction of original ground by mechanical means including filling in depression occuring during rolling including cost of all labour, HOM complete as per specifications.and as per the directions of the Engineer-in-charge	Sqm	2347.64	2347.64	100	27-04-21	15-05-21	18
15	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/ trap/basalt material, mixing in a mechanical mix plant at OMC, Carriage of mixed	Cum	341.28	341.28	100	03-05-21	23-05-21	20
16	Cement concrete pavement.Construction of un-reinforced plain cement concrete pavement, using a grade concrete M30 over a prepared base with OPC coarse aggregate @ 0.69cum fine aggregate @ 0.46cum,coarse and fine aggregate	Cum	352.15	352.15	100	08-05-21	30-05-21	22

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

MAHANAGARA PALIKE

rrounding area roads in ward no 06 Thanisandra

Jan-21	Feb-21	Mar-21	Apr-21	May-21	Jun-21

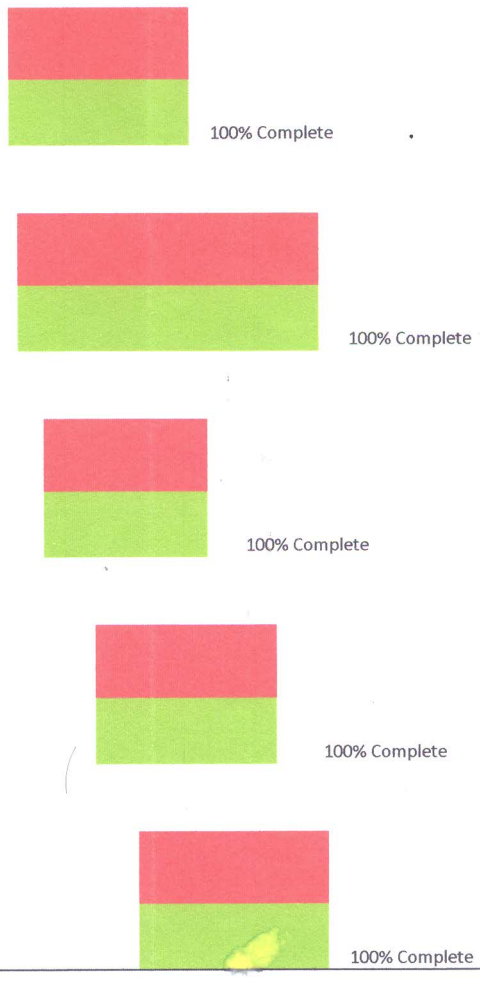

LEGEND

= Planned %

= Executed

ಪಾಲಿಕೆ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿಬಿಎಂಪಿ, ಬೆಂಗಳೂರು-24

CIVIL Pro
Sig.....
Date.....
BANGALORE
